


Stage 4: Hunter Rd/Greenwood Ave June – August 2022

Arrows denote the sidewalk is open for users and the travel direction to nearby schools

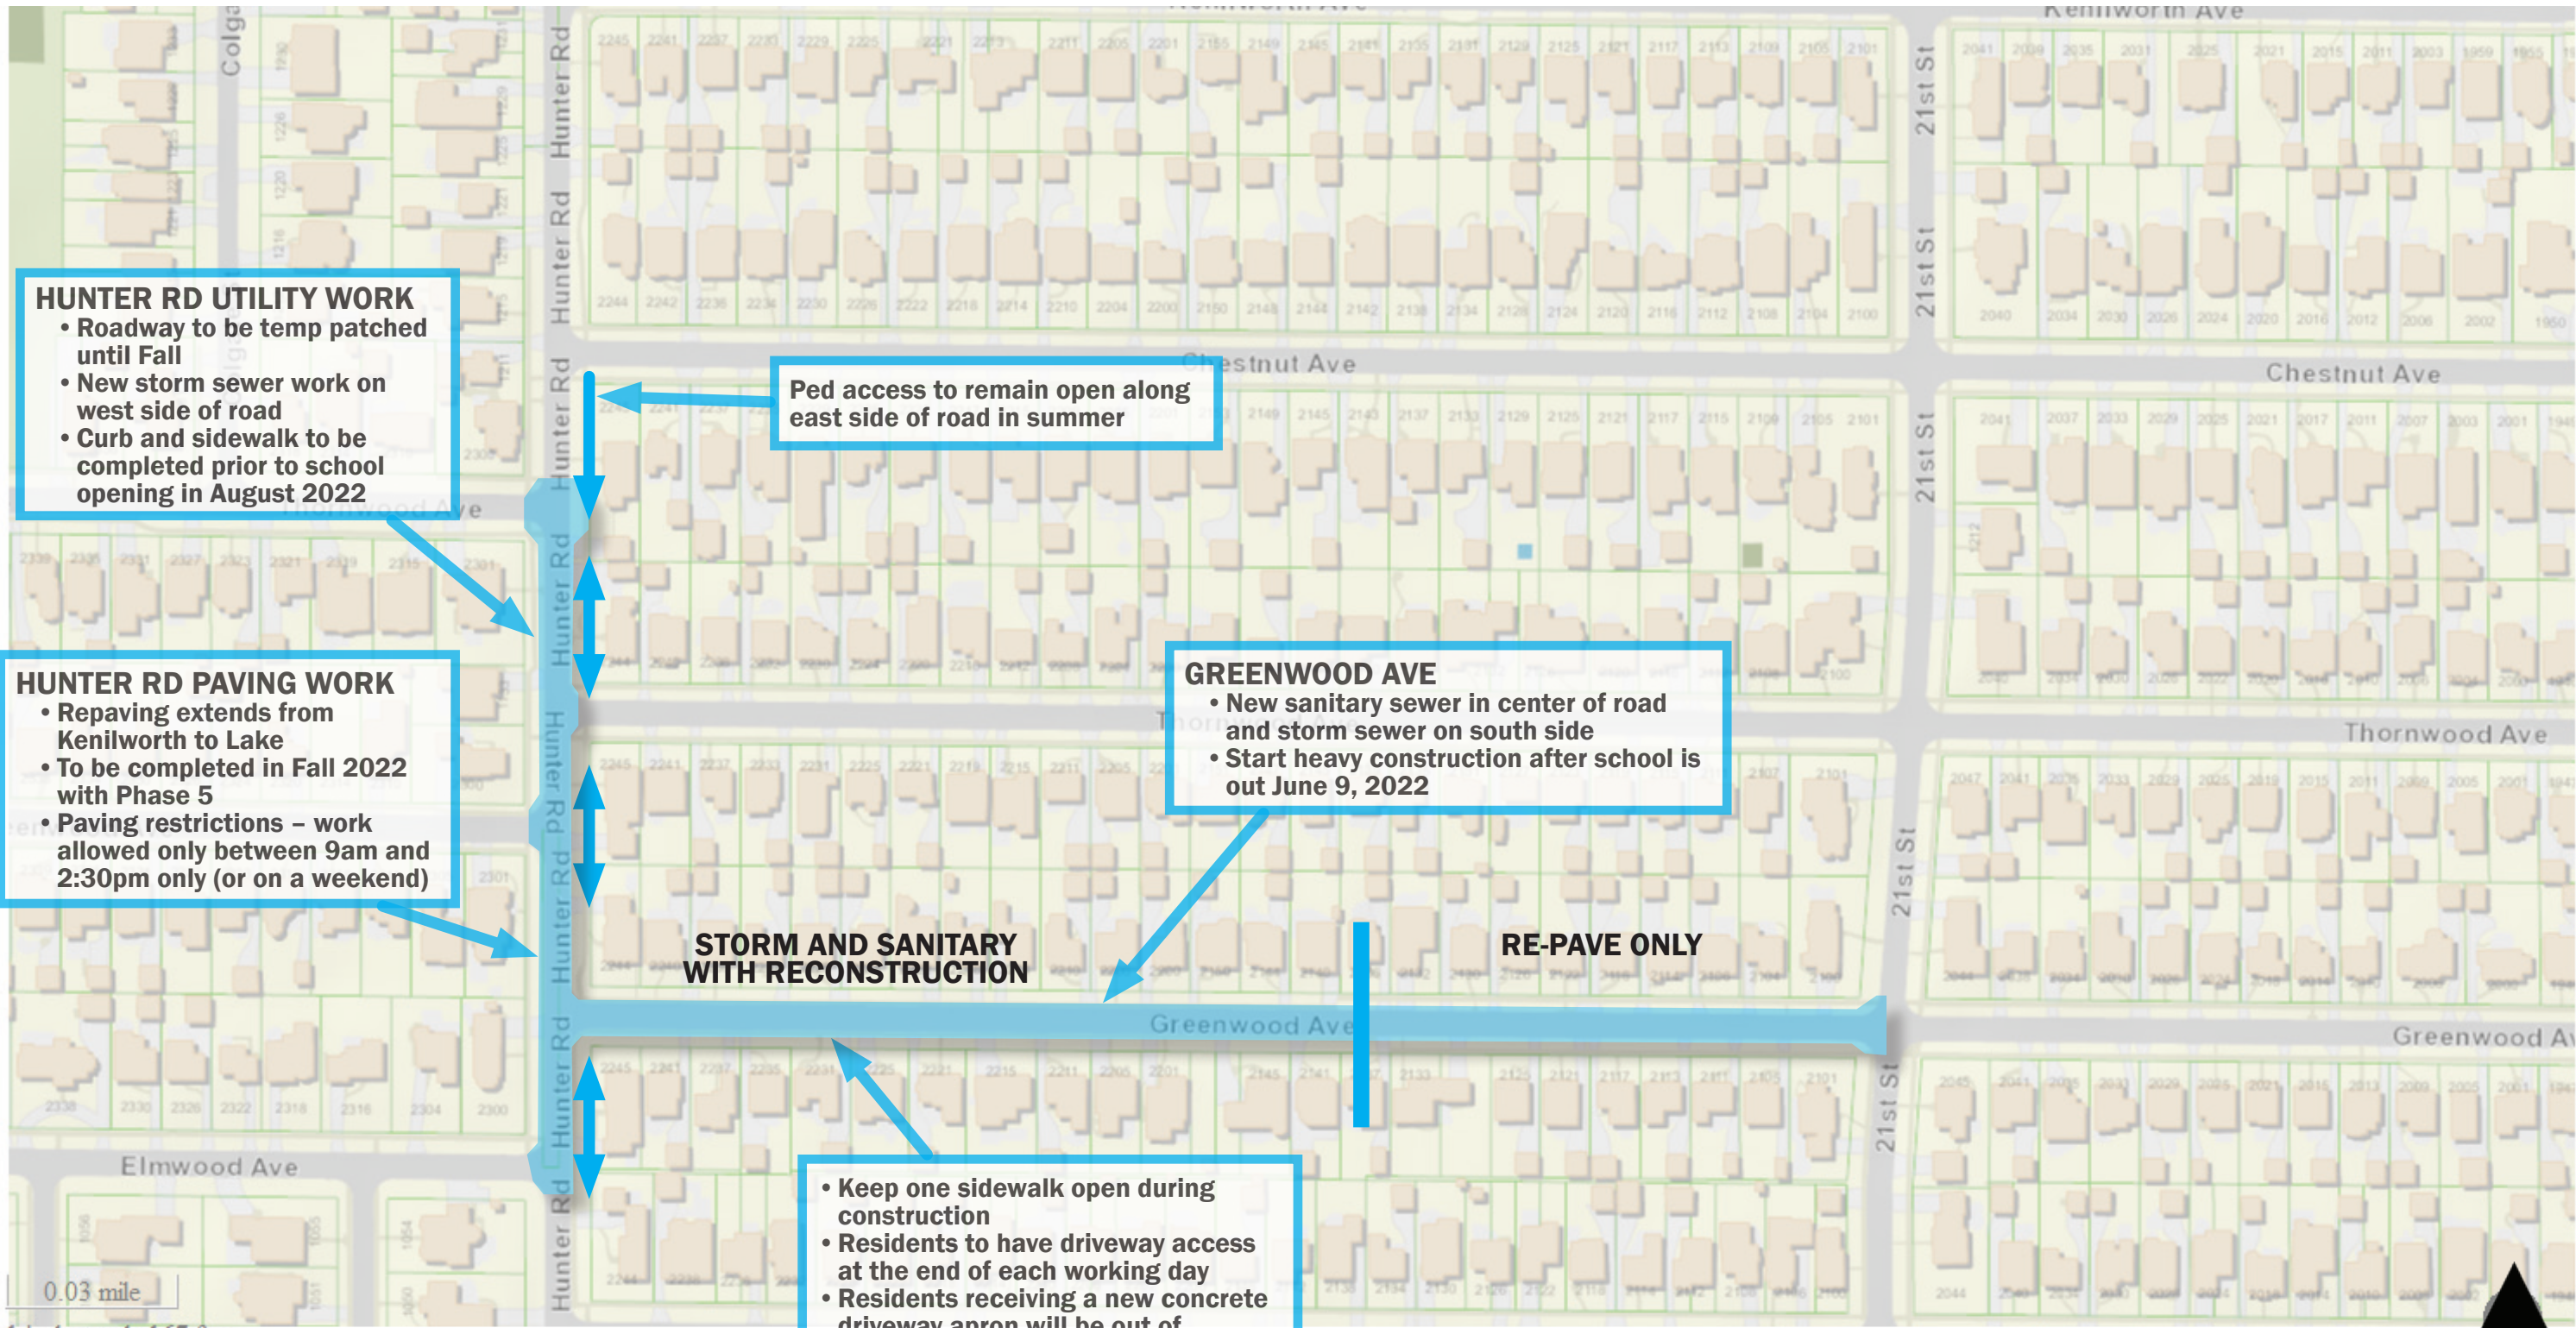

HUNTER RD UTILITY WORK

- Roadway to be temp patched until Fall
- New storm sewer work on west side of road
- Curb and sidewalk to be completed prior to school opening in August 2022

Ped access to remain open along east side of road in summer

GREENWOOD AVE

- New sanitary sewer in center of road and storm sewer on south side
- Start heavy construction after school is out June 9, 2022

HUNTER RD PAVING WORK

- Repaving extends from Kenilworth to Lake
- To be completed in Fall 2022 with Phase 5
- Paving restrictions – work allowed only between 9am and 2:30pm only (or on a weekend)

STORM AND SANITARY WITH RECONSTRUCTION

RE-PAVE ONLY

- Keep one sidewalk open during construction
- Residents to have driveway access at the end of each working day
- Residents receiving a new concrete driveway apron will be out of their driveways for a cure time of approximately 7-10 days



0.03 mile
